



2nd Progress Update -

- Unfortunately the Respite Rooms have encountered a few supply delays so they are now looking to be completed mid July.
- **Stage 2 – Independent Living – Units.** The framing of all 3 duplex units have been erected and Unit 3's roof is to be added in the next few days. The Drainage work was completed this week, a challenging job with the wet weather!
- **Stage 3 – Upgrading of existing Home.** The internal painting of the Home is coming along well and looking very smart. We have received notification that the 1st batch of wool carpet tiles are now available so we hope to have these laid in the dining room, being the first area, by mid July. The dining room will then join the list of completed tasks.
- The reroofing is making a huge impact on the exterior look of Hillview, what a difference!!, it is hoped that this will be completed by the end of next week.

The Board have received many pleasing comments regarding PROJECT HILLVIEW and it's progress, the community are thrilled to see positive happenings in our district.

If you able to help us reach our funding target of \$4M please contact Claire Grainger, Board Chairperson or Tanya Lindsay, Hillview General Manager – DONATIONS ARE APPRECIATED!




Reroofing commenced




Removing the small area of asbestos – How lucky we were!



New Roof

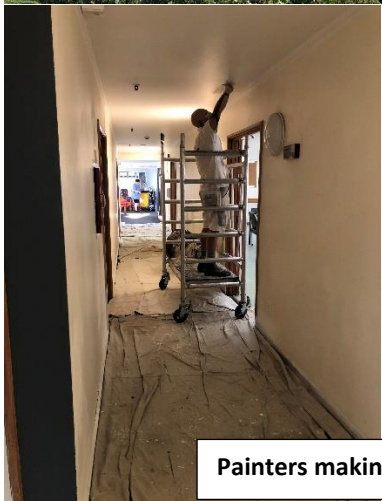

Painters making great progress

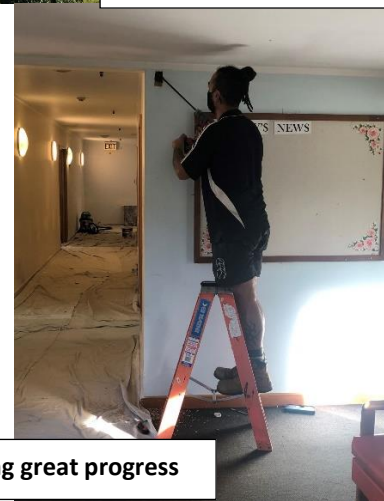

Drainage complete



Framing up for Units



Regards Claire Grainger – Hillview Trust Board Chairperson
